CONDTION DISCHARGE

20 EARNING STREET GODMANCHESTER HUNTINGDON PE29 2DJ

22/02262/LBC– Approved Mon 20 Feb 2023


3. Condition. No brickwork shall be laid until a sample brick panel of 1m2 has been prepared on site illustrating the choice of brick, bond, mortar mix, colour, design and pointing technique and the details have been submitted to and approved in writing by the Local Planning Authority. The approved sample panel is to be retained on site for the duration of the works for comparative purposes, and works will take place only in accordance with approved details.

4. Condition. Following the demolition of the existing wall but prior to the construction of the new wall, hereby approved, a 1:5 sectional detail of the wall head and coping shall be submitted to and approved in writing by the Local Planning Authority.

Materials :

The Brick used was Cawarden 76mm Reclaim Derby Orange in the below sample
Mortar mix was a 5:1 sand and cement (White Cement)

The wall is proposed to be 1900mm high as per the approved drawing reference 22241/02 rev B.

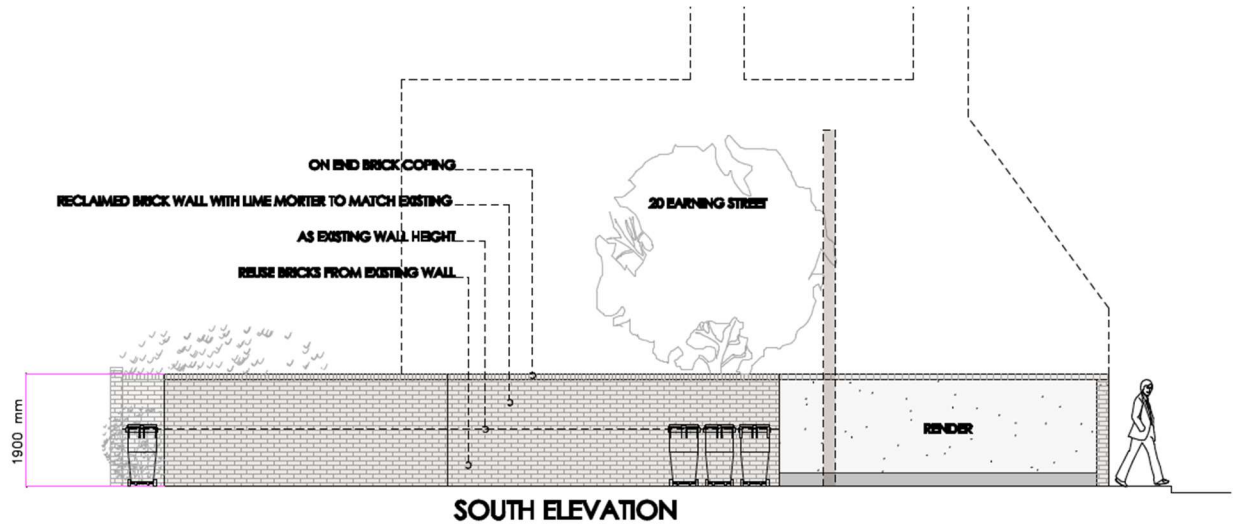



The existing brick type can be seen behind. This panel is on site for review.




Photo of wall with brick on edge capping to be replicated

Brick Bond :

The type of the existing wall is a Stretcher / running bond with brick on edge to the top this will be replicated


Brick Pointing type :

The existing wall has a raked finish to the pointing to be replicated . raked style with a 12mm inset.

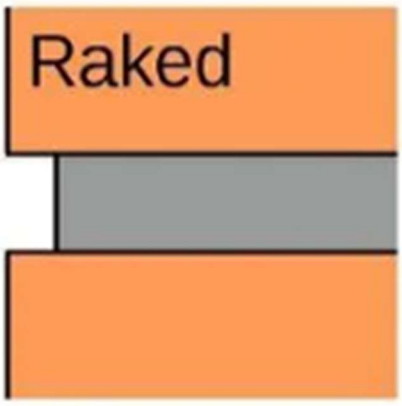

Detail :

See below for the construction of the wall with the coursing and thickness with wall ties and a foundation. A 1:5 detail has been provided of the below image

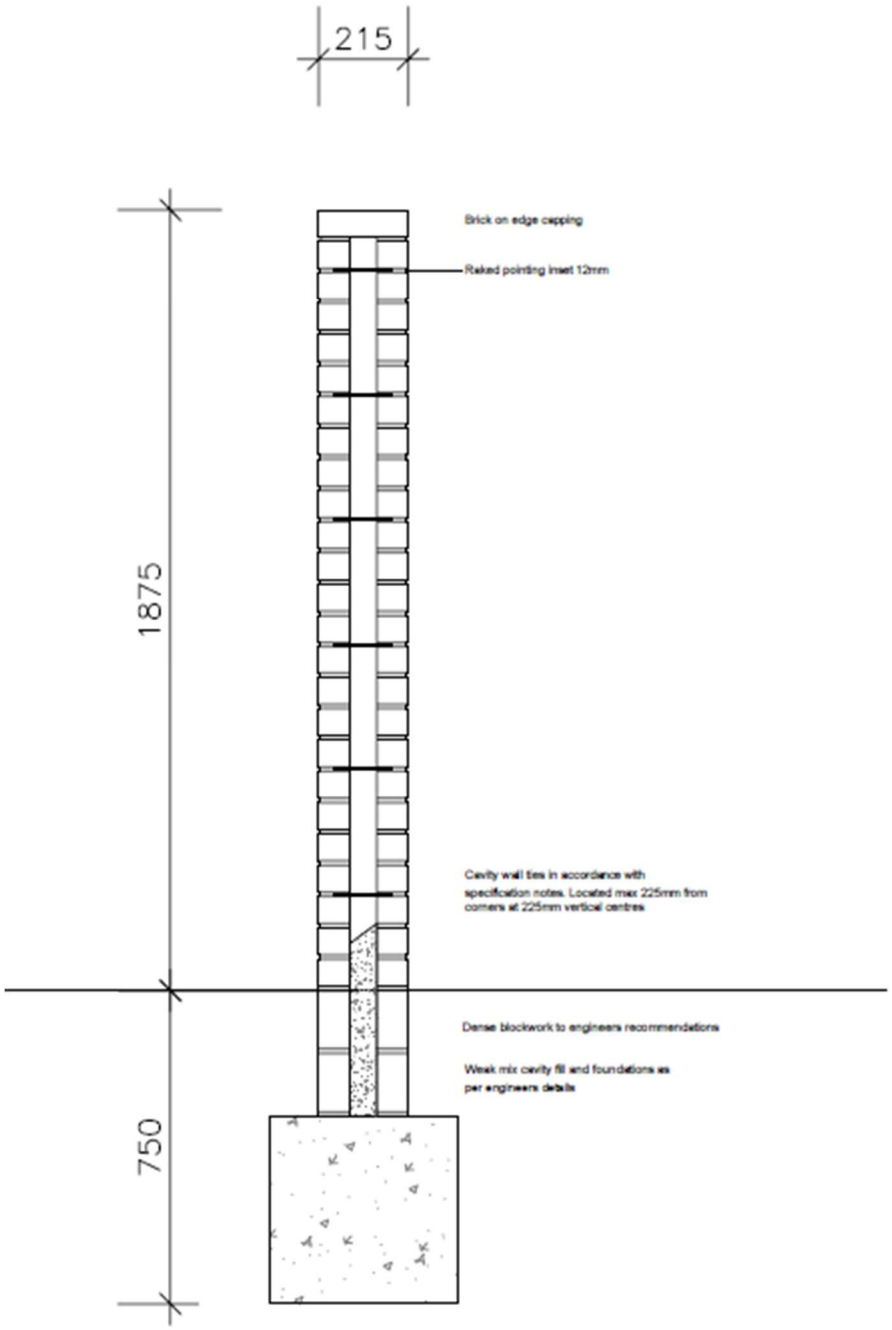

Mtaylor

13-6-2025
