METHOD STATEMENT for TREE MANAGEMENT and PROTECTION

PURPOSE

This Arboricultural Method Statement describes how this part complete Consented development will be planned to avoid any damage to retained trees and address the concerns raised over recent operations that may have affected the trees.

TEAM DETAILS


ROLE	NAME	EMAIL/ TELEPHONE
DEVELOPER	• Andrew Sincock	•
MAIN CONTRACTOR	•	•
SITE MANAGER	•	•
PROJECT ARBORICULTURALIST	• Andrew Belson	•
TREEWORK CONTRACTOR	•	•
LOCAL AUTHORITY TREE OFFICER	•	•
DESIGNER	•	•
	•	•
	•	•
	•	•
	•	•
	•	•

INSPECTION AND MONITORING SCHEDULE

KEY EVENT	ARBORICULTURAL ACTIVITY	TIMING	DATE COMPLETED	SITE MANAGER'S SIGNATURE
Site preparation	Inspect cleared ground by video call	Before ground protection is laid		
Tree protection measures	Inspect barriers and ground protection by video call	Before construction recommences		
Check barriers and signage	Ongoing site responsibility	During construction		
Construction of driveway	Monitoring and supervision	During construction		
Remove barriers	Inspect trees and specify remedial work.	Post construction		
Check for soil compaction	Agree ground condition with HDC Arboricultural Officer	Post construction		
ADDITIONAL				

Post-completion all arboricultural works can be signed off below:

Arboricultural Consultant:	Site Manager:
Signature:	Signature:

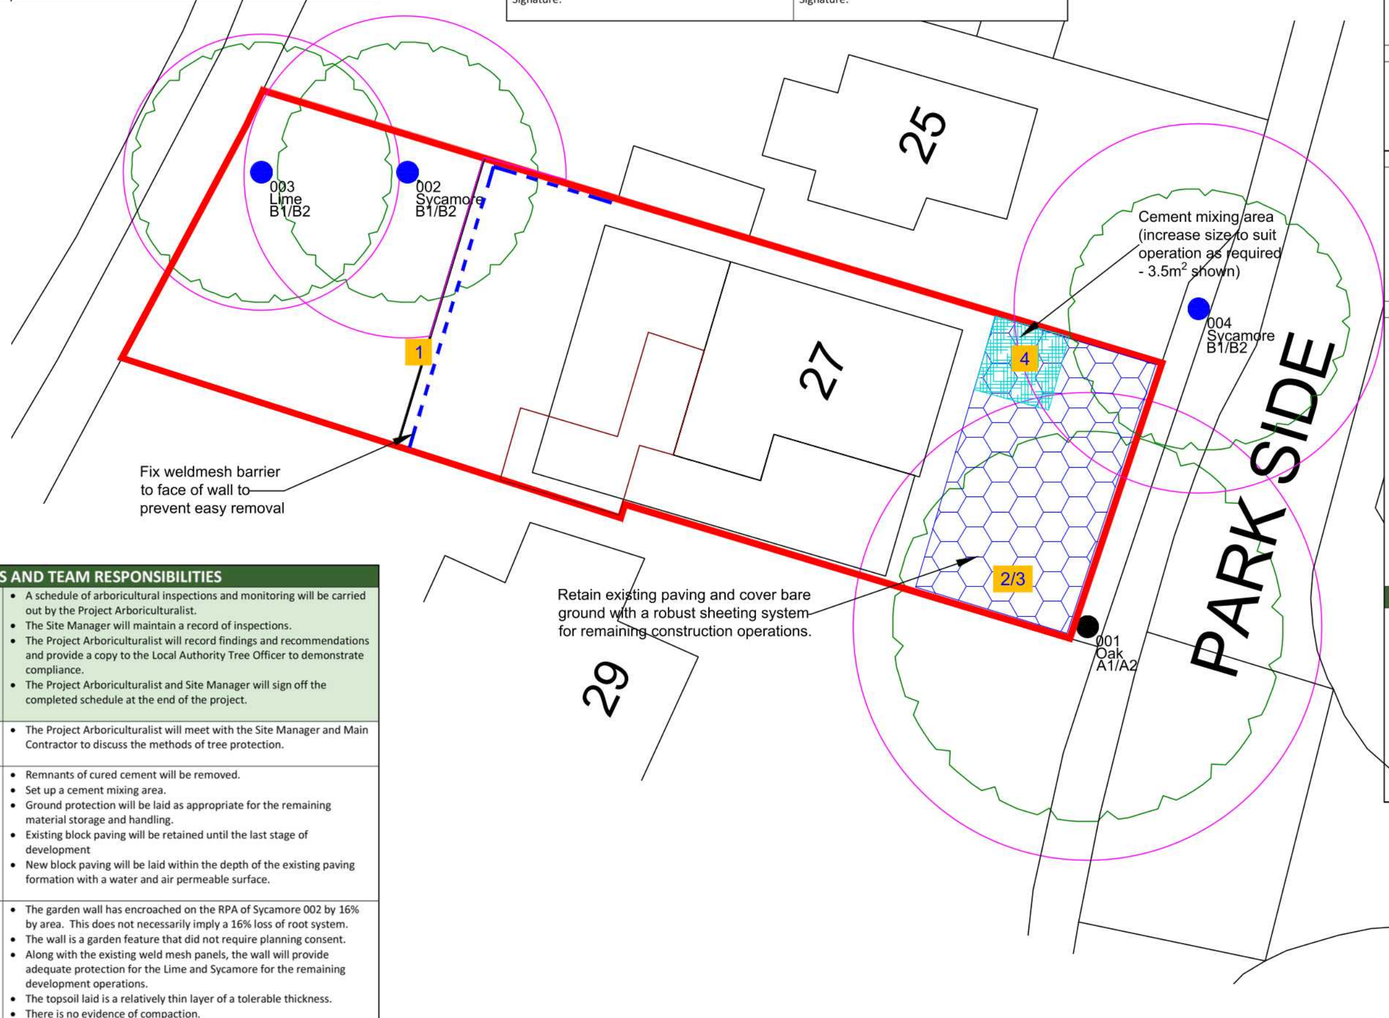

SEQUENCE OF ACTIVITIES AND TEAM RESPONSIBILITIES

THROUGHOUT:		• A schedule of arboricultural inspections and monitoring will be carried out by the Project Arboriculturalist. • The Site Manager will maintain a record of inspections. • The Project Arboriculturalist will record findings and recommendations and provide a copy to the Local Authority Tree Officer to demonstrate compliance. • The Project Arboriculturalist and Site Manager will sign off the completed schedule at the end of the project.
RE-COMMENCEMENT SITE MEETING		• The Project Arboriculturalist will meet with the Site Manager and Main Contractor to discuss the methods of tree protection.
CONSTRUCTION	FRONT AREA Issues: • Possible contamination • Materials storage	• Remnants of cured cement will be removed. • Set up a cement mixing area. • Ground protection will be laid as appropriate for the remaining material storage and handling. • Existing block paving will be retained until the last stage of development • New block paving will be laid within the depth of the existing paving formation with a water and air permeable surface.
	REAR AREA Issues: • Impact of garden wall • Preparation for turfing, including the laying of topsoil • Barrier location	• The garden wall has encroached on the RPA of Sycamore 002 by 16% by area. This does not necessarily imply a 16% loss of root system. • The wall is a garden feature that did not require planning consent. • Along with the existing weld mesh panels, the wall will provide adequate protection for the Lime and Sycamore for the remaining development operations. • The topsoil laid is a relatively thin layer of a tolerable thickness. • There is no evidence of compaction.
POST-CONSTRUCTION		• Once the main construction activities are complete the protective barriers and any ground protection will be removed before landscaping work begins. • The Project Arboriculturalist will inspect the trees on and adjacent to the site and identify any remedial works that might be required. • A schedule of works will be produced (where necessary) and circulated to the Local Authority Arboriculturalist for approval. • The Tree Work Contractor will implement the works. • The Project Arboriculturalist will sign off the works and produce a Completion Certificate to the Local Authority Arboriculturalist.

STAGE 1 ENABLING WORKS

NO.	MATERIALS	NOTES
1	Weldmesh panels on offset support blocks with lateral struts	The existing weldmesh barriers will be maintained on their current line where shown by the dashed blue lines on the Tree Protection Plan (see notes on barriers below)
2	Plywood sheets or a hired-in ground protection sheeting system	Ground at the front of the site will be protected by a combination of existing paving and/or a double-layer of (minimum 16mm) plywood sheeting before any further construction operation or any materials are brought on site. The area for ground protection is shown by the blue hexagonal hatch on the drawing.
3	Cellular confinement geoweb and no-fines aggregate	To construct the front drive, the area denoted by the blue hexagonal hatch will be paved within the depth of the existing block paving, its base and sub-base. The new sub-base will be constructed with the use of a cellular confinement system and finished with a water and air permeable surface. (see Notes on construction of access and parking bays below)
4	Impervious sheeting such as DPM or butyl rubber	For any remaining operations that require the mixing of materials that contain cement, a catchment area will be set up to prevent any water or cement-based products from coming into contact with the ground.

GENERAL PRINCIPLES OF SITE MANAGEMENT FOR TREE PROTECTION

- No fires will be lit on site
- No storage or discharge of materials unless on the prepared ground protection.
- The mixing of cement and dispensing of fuel or chemicals will only be carried out within the designated area.
- Any damage that occurs to the trees during construction will be rectified to BS3998: 2010.
- Trees must not be used as anchor points for winching or for supporting wires/cables.

REMOVAL OF SUPERFICIAL CONTAMINANTS

- All materials, barriers and spoil will be removed from the front of the site area.
- Any spilt materials containing cement will be carefully removed by hand, using hand tools only.
- The cleaned site will be inspected by the Project Arboriculturalist before the ground protection is laid.

BARRIERS

- Weather-proof notices stating: 'PROTECTED AREA – DO NOT ENTER' to be erected on barriers not less than 5m apart. (example on plan)
- Barriers will remain in place until the end of the main construction period.

SUITABLE HIRED-IN GROUND PROTECTION SYSTEMS

- LIVE (formerly Eve) provide Trakway access systems in timber, aluminium or plastic for a variety of potential loads. See http://www.livetrakway.com for more details or call 08700 76 76 76).
- Alternatively, Ground-Guards provide a range of ground protection mats from lightweight to heavy-duty. See http://www.ground-guards.co.uk for more details or call 0113 267 6000).

INSTALLATION OF SERVICES


- The default location for any trenching for the installation of services or other excavations for soakaways etc. will be located at least 1m from the radial extent of the RPAs drawn.
- Any further excavations for services inside Root Protection Areas will be carried out under arboricultural supervision.
- Any roots found will be worked around where practical.
- Any damaged roots will be pruned back to a suitable union by the Project Arboriculturalist using a sharp hand saw or by-pass secateurs.

CONSTRUCTION OF DRIVEWAY

- Once all materials handling and mixing of products containing cement has finished, the ground protection sheeting will be removed.
- The area for paving will be excavated no deeper than the cumulative depth of the existing block paving, to include the sand bed and any sub-base.
- A filter membrane such as 'Terram 1000' will be laid over the excavated area.
- A cellular confinement geoweb of 150mm profile will be laid over the membrane. Options include. Options include:
  - The Geoweb® Tree Root Protection System offered by Greenfix UK (see http://greenfix.co.uk for more details or call 01608 666027).
  - Cellweb® Tree Root Protection (TRP) from Geosynthetics Limited (see http://www.geosyn.co.uk or call 01455 617 139)
- The driveway edgings will be formed with timber edging boards supported by driven stakes.
- The cellular confinement system will be backfilled with 20-40mm no-fines graded stone and compacted, adding more aggregate as necessary to bring to level.
- The prepared surface will be finished with a water and air permeable surface such as Marshalls 'Priora, installed with the manufacturer's permeable grout.

POST CONSTRUCTION

- Once all the construction and hard landscaping works are completed and all plant and machinery has been taken off site, the protective barriers and ground protection will be removed before landscaping work begins.
- The ground will be re-tested for compaction through a joint meeting between the HDC Arboriculturalist and the Project Arboriculturalist.
- If required, a programme of de-compaction will be agreed and carried out when ground conditions are optimal.
- Soil cultivation within the previously protected zones will be carried out by hand only. No machine cultivation will take place within these zones whatsoever.
- Planting within the previously protected zones will be carried out by hand using hand tools only.
- Retained trees will be re-inspected post-development by a qualified arboriculturalist and any works arising carried out within the time limits specified.



This drawing is the property of Andrew Belson Arboricultural Consultant. Copyright is reserved by him and the drawing is issued on the condition that it is not copied, reproduced, retained or disclosed to any unauthorised person either wholly or in part without the consent of Andrew Belson.

NOTES Based on block plan 1152

The original of this drawing was produced in colour - a monochrome copy should not be relied upon.

KEY

- ROOT PROTECTION AREA
- CANOPY OUTLINE - INDIVIDUAL TREE
- IMMOVEABLE WELD MESH BARRIER
- AREA PROTECTED WITH ROBUST SHEETING UNTIL THE END OF THE MAIN CONSTRUCTION PHASE THEN SURFACED WITHIN DEPTH OF PREVIOUS BLOCK PAVING WITH GEOWEB SUB-BASE
- INDICATIVE CEMENT MIXING AREA TO BE CONSTRUCTED WITH IMPERVIOUS SHEETING

Rev	Description	Date
B	AMS amended	13.08.25
A	Sycamore 004 added	11.07.25

Purpose of Issue
Planning

Andrew Belson Ltd
Arboricultural Consultant
AA Registered Consultant
The Tree House, 1a First End
Station Road, Uppingham
Oakham LE15 9TX
t: 01572 823637
e: info@belsontreesurvey.co.uk

Client

Mr A Sincock

Project

27 Parkside, Little Paxton
St Neots PE19 6NW

Drawing Title
ARBORICULTURAL METHOD STATEMENT AND TREE PROTECTION PLAN

Drawn	Checked	Reviewed	Date
AMB	--	--	13/08/2025
Job No.	Scale	Sheet Size	Revision
5825	1:200	A2	B

Drawing Number
5825.Little Paxton.Sincock.TPP
